







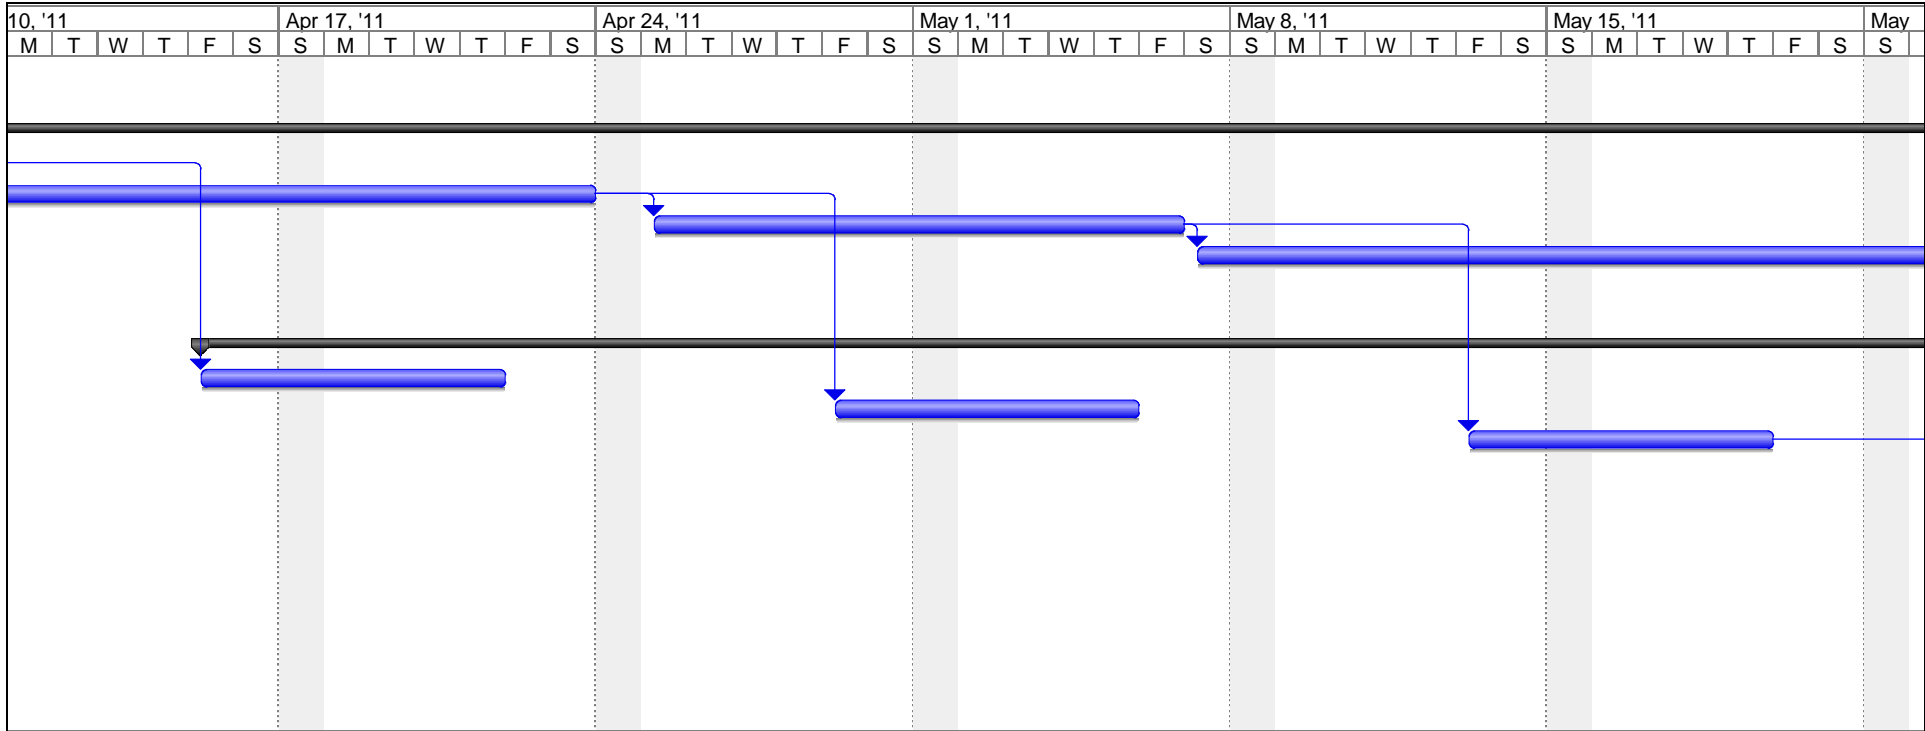

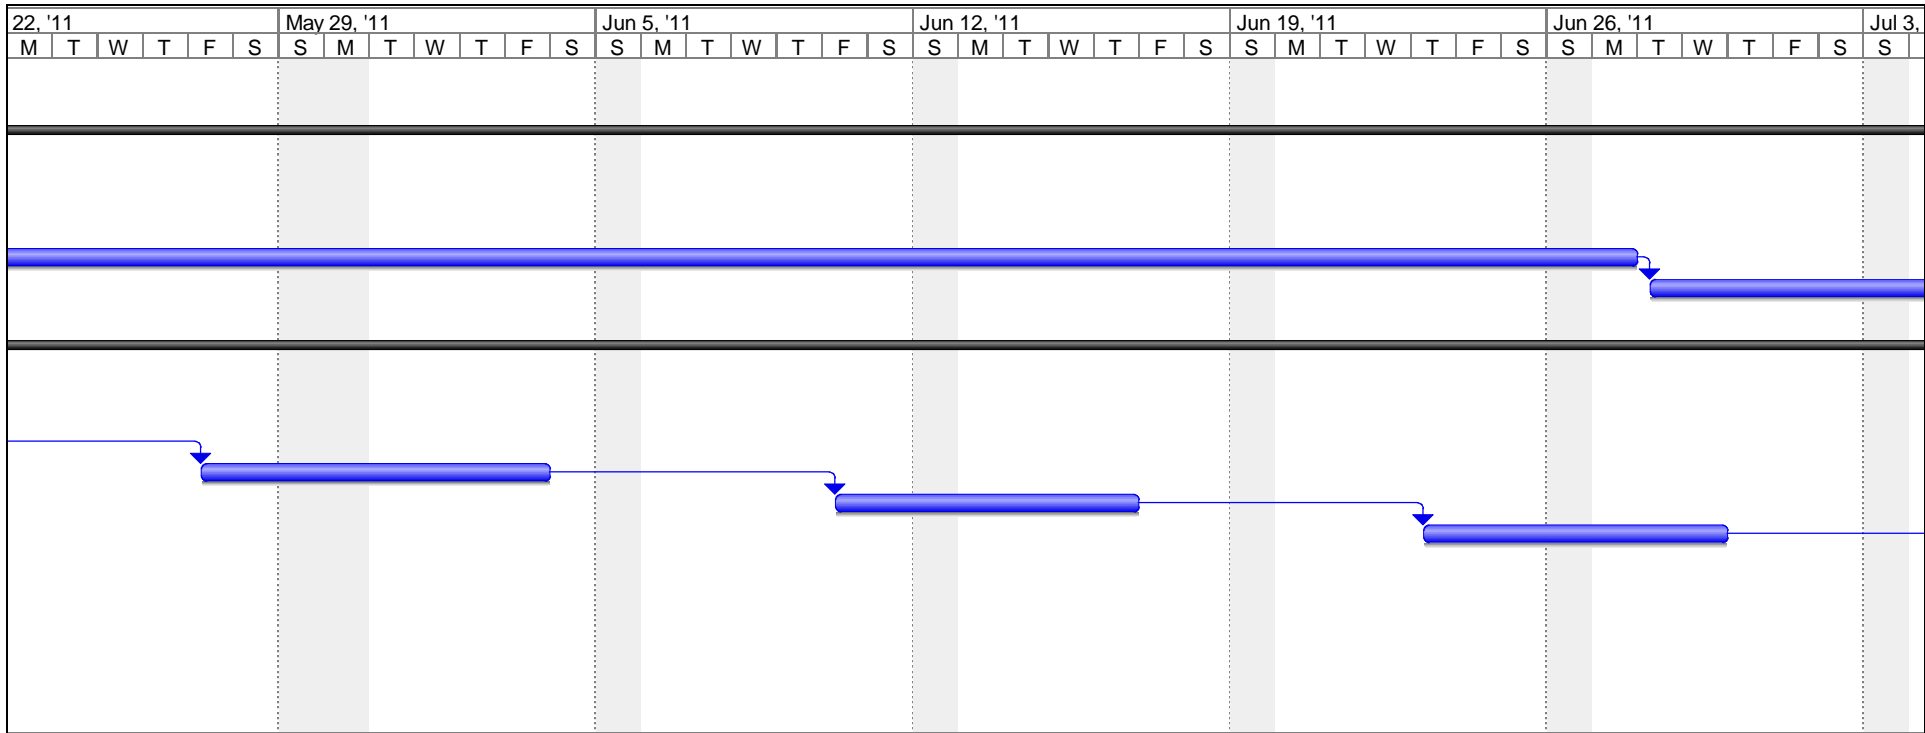


ID	Task Name	Duration	Start	Finish	Mar 27, '11							Apr 3, '11							Apr 10
					S	M	T	W	T	F	S	S	M	T	W	T	F	S	S
1	Mobilization	6 days	Mon 3/28/11	Sat 4/2/11															
2	Mobilize equipment and resources	6 days	Mon 3/28/11	Sat 4/2/11															
3	River Dredge Progression	90 days	Mon 4/4/11	Tue 7/19/11															
4	Progression 1 - LR Grid 315-278	5 days	Mon 4/4/11	Fri 4/8/11															
5	Progression 2 - LRRR Grid 254-198	13 days	Sat 4/9/11	Sat 4/23/11															
6	Progression 3 - LRRL Grid 235-189	11 days	Mon 4/25/11	Fri 5/6/11															
7	Progression 4 - IHBBRL Grid 183-111	43 days	Sat 5/7/11	Mon 6/27/11															
8	Progression 5 - IHBBRR Grid 194-118	17 days	Tue 6/28/11	Mon 7/18/11															
9	Progression 6 - LR Deposit 3	1 day	Tue 7/19/11	Tue 7/19/11															
10	Sediment Loading, T&D	83 days	Fri 4/15/11	Fri 7/22/11															
11	Load-out Phase 1	6 days	Fri 4/15/11	Thu 4/21/11															
12	Load-out Phase 2	6 days	Fri 4/29/11	Thu 5/5/11															
13	Load-out Phase 3	6 days	Fri 5/13/11	Thu 5/19/11															
14	Load-out Phase 4	6 days	Fri 5/27/11	Fri 6/3/11															
15	Load-out Phase 5	6 days	Fri 6/10/11	Thu 6/16/11															
16	Load-out Phase 6	6 days	Thu 6/23/11	Wed 6/29/11															
17	Load-out Phase 7	6 days	Wed 7/6/11	Tue 7/12/11															
18	Load-out Phase 6	5 days	Mon 7/18/11	Fri 7/22/11															
19	Mitigation	12 days	Wed 7/20/11	Tue 8/2/11															
20	Additional sediment removal or cover	12 days	Wed 7/20/11	Tue 8/2/11															
21	De-mobilization	10 days	Wed 8/3/11	Sat 8/13/11															
22	De-mobilize equipment, dewatering area, and resources	10 days	Wed 8/3/11	Sat 8/13/11															


Project: Project Schedule Date: Wed 12/1/10	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Project Schedule Date: Wed 12/1/10	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Project Schedule Date: Wed 12/1/10	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

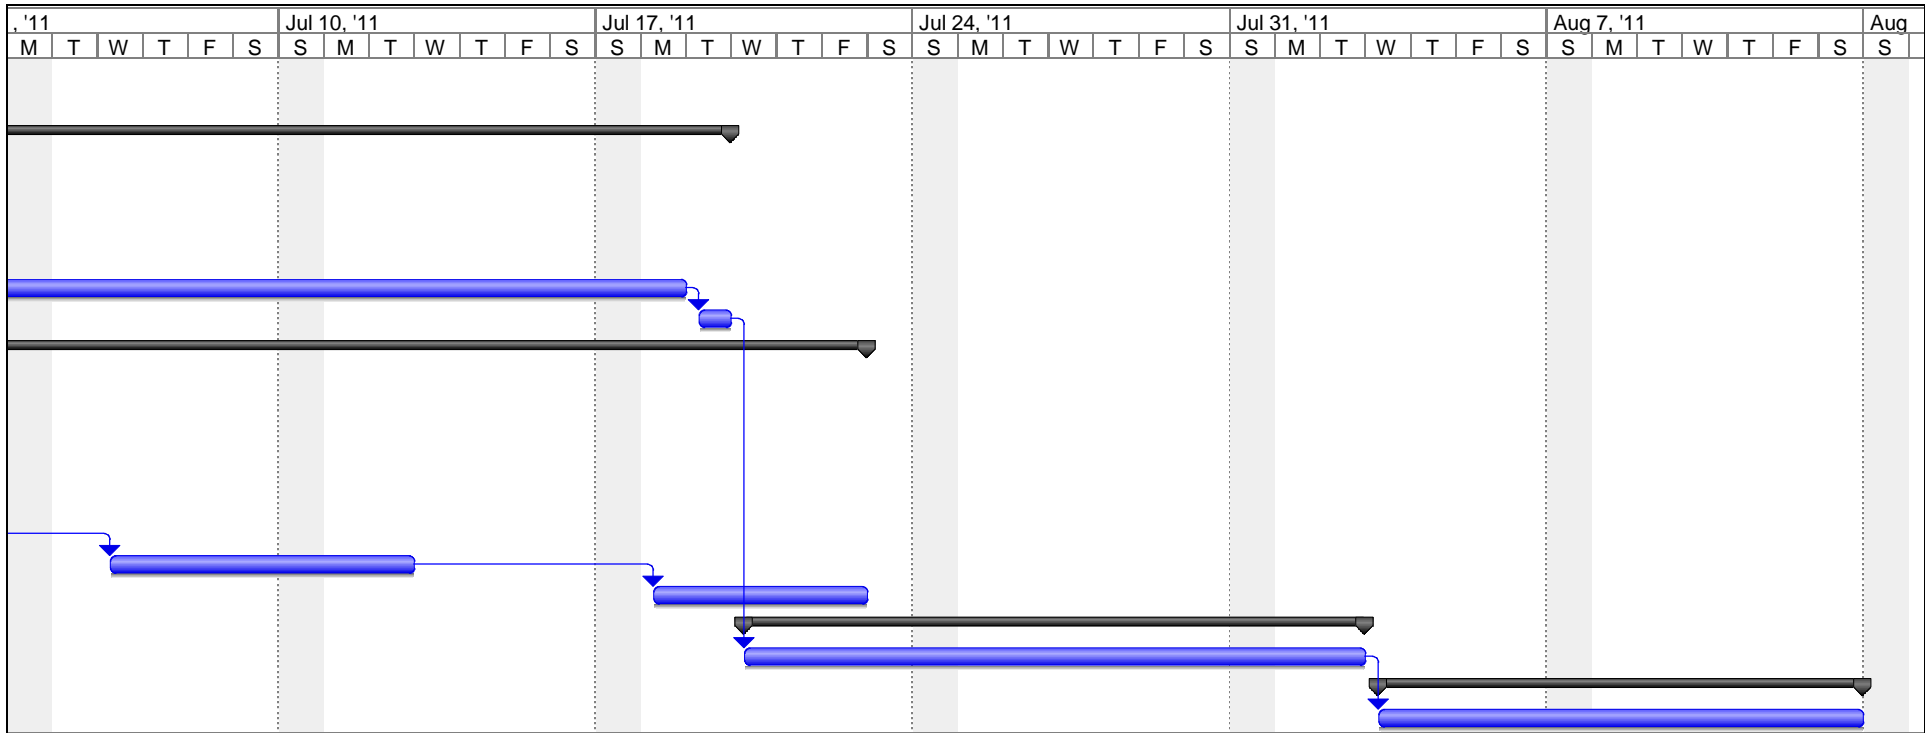

Project: Project Schedule Date: Wed 12/1/10	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
